



# GURNER™

GROUP

189 KENT STREET SYDNEY

CUSTOMISATIONS TRACKER

MARCH 2026



189 Kent Street  
SALUS PLACE — CUSTOMISATIONS TRACKER

SKETCHES ISSUED 11/21  
PENDING SKETCHES 2  
TODAY 13 Mar 2026

OVERVIEW UNITS & ACTIONS GANTT CHART PHASES & MILESTONES



Ball in Court



Customisations — Design Progress

|            |                          |           |                                                |     |    |
|------------|--------------------------|-----------|------------------------------------------------|-----|----|
| O80IS      | Socorro Wescott          | Diamond   | 1.1 Sketch Plan Issued                         | 15% | DW |
| O802S      | Socorro Wescott          | Diamond   | 1.1 Sketch Plan Issued                         | 15% | DW |
| O90IS      | John Corollo             | Diamond   | 1.1 Sketch Plan Issued                         | 15% | ED |
| 1202S      | Tom Lin                  | Diamond   | 1.1 Sketch Plan Issued                         | 15% | GD |
| 170IS      | Hani Sedaris             | Diamond   | 1. Written Brief Due / Design Breifing Session | 8%  | ED |
| 190I/1902S | Marco Hara               | Penthouse | 1.1 Sketch Plan Issued                         | 15% | DW |
| 200I/2002S | Property Holdings N...   | Penthouse | 1.1 Sketch Plan Issued                         | 15% | DW |
| 210I/2102S | Jack Davis Rico          | Penthouse | 1.1 Sketch Plan Issued                         | 15% | DW |
| 210IN      | Denise Azzi (Charlie ... | PH Custom | 1.1 Sketch Plan Issued                         | 15% | GD |
| 250IS      | Damian Hanna             | Penthouse | 1. Written Brief Due / Design Briefing Session | 3%  | DW |

**GURNER™**

## SALUS PLACE – CUSTOMISATIONS TRACKER

OVERVIEW

UNITS & ACTIONS

GANTT CHART

PHASES & MILESTONES

STATUS:

ALL

EXCHANGED

ISSUED

BESPOKE:

ALL

YES

NO

BIC:

ALL

DW

ED

GD

WM

| UNIT       | PURCHASER                              | AGENT           | SPEC SHEET | STATUS    | BIC | AMALG | BESPOKE | F&F | PLAN | COMMS | EXCHANGED DATE | CUR. STATUS                        | NEXT STEPS                                                                                                                                                                                      |
|------------|----------------------------------------|-----------------|------------|-----------|-----|-------|---------|-----|------|-------|----------------|------------------------------------|-------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|
| 0701S      | Virginia Nemeth                        | Apex            | Diamond    | EXCHANGED | —   | —     | —       | ✓   |      | —     | 04 Feb 26      | 11 Sketch Plan Issued              | Setup in person design meeting, to finalize finishes and any design comments                                                                                                                    |
| 0702S      | Virginia Nemeth                        | Apex            | Diamond    | EXCHANGED | —   | —     | —       | ✓   | —    | —     | 04 Feb 26      | —                                  | no request issued, letter                                                                                                                                                                       |
| 0801S      | Socorro Wescott                        | Apex            | Diamond    | EXCHANGED | DW  | —     | ✓       | ✓   |      |       | 04 Dec 25      | 11 Sketch Plan Issued              | 11/03/26_DW to email letter, confirming layout                                                                                                                                                  |
| 0802S      | Socorro Wescott                        | Apex            | Diamond    | EXCHANGED | DW  | —     | ✓       | ✓   |      | —     | 04 Dec 25      | 11 Sketch Plan Issued              | 11/03/26_DW to email letter, confirming layout                                                                                                                                                  |
| 0901S      | John Corallo                           | APEX            | Diamond    | EXCHANGED | ED  | —     | ✓       | ✓   |      | —     | 28 Oct 25      | 11 Sketch Plan Issued              | Setup in person design meeting, to finalize finishes and any design with purchaser, confirm layout                                                                                              |
| 1002S      | Michael Dakhoul & Houda Dakhoul        | The Agency      | Diamond    | EXCHANGED | —   | —     | —       | —   | —    | —     | 24 Dec 25      | —                                  | —                                                                                                                                                                                               |
| 1202S      | Tom Lin                                | The Agency      | Diamond    | EXCHANGED | GD  | —     | ✓       | —   |      | —     | 06 Nov 25      | 11 Sketch Plan Issued              | Changes marked up.Gurner Design to update drawing. Include la remotely due to overseas buyer. (C) enlarged ensuite to accommodate butlers kitchen being opened to living area to accommodate on |
| 1402N      | Michael Bourke                         | The Agency      | Diamond    | EXCHANGED | —   | —     | —       | —   |      | —     | 27 Oct 25      | —                                  | —                                                                                                                                                                                               |
| 1701S      | Hani Sedaris                           | The Agency      | Diamond    | EXCHANGED | ED  | —     | ✓       | —   |      | —     | 22 Sept 25     | 1 Written Brief Due / Design Brief | Elle to liaise with The Agency to setup design meet. Follow up with                                                                                                                             |
| 1901/1902S | Marco Hara                             | The Agency      | Penthouse  | EXCHANGED | DW  | ✓     | ✓       | ✓   |      |       | 10 Oct 25      | 11 Sketch Plan Issued              | 09/03/26 WM issued draft letter to Deb. Once signed off WM to                                                                                                                                   |
| 1901N      | Peter Ping Xie and Xiao Ling Shen W... | APEX            | Penthouse  | EXCHANGED | DW  | —     | —       | ✓   |      | —     | 29 Sept 25     | 11 Sketch Plan Issued              | 11/3/26 Deb to follow up with Apex on Status of Design. 11/03/26 coordinate into documentation for Pricing.                                                                                     |
| 2001/2002S | Property Holdings No 2 Pty Ltd         | The Agency      | Penthouse  | EXCHANGED | DW  | ✓     | ✓       | ✓   |      | —     | 15 Oct 25      | 11 Sketch Plan Issued              | Deb to send email to agent confirming the current status of the ε                                                                                                                               |
| 2101/2102S | Jack Davis Rice                        | The Agency      | Penthouse  | EXCHANGED | DW  | ✓     | ✓       | ✓   |      | —     | 11 Oct 25      | 11 Sketch Plan Issued              | Deb to send email to agent confirming the current status of the ε                                                                                                                               |
| 2101N      | Denise Azzi (Charlie Ayoub)            | The Agency      | PH Custom  | EXCHANGED | GD  | —     | ✓       | —   |      | —     | 19 Feb 26      | 11 Sketch Plan Issued              | Gurner design team working through layout design update. Issu                                                                                                                                   |
| 1001N      | Domenico Cece & Teresa Maria Cece      | Inspired Wealth | —          | ISSUED    | WM  | —     | —       | —   |      | —     | —              | 11 Sketch Plan Issued              | 09/03/26 WM has issued to WT for pricing, due 12/03/26                                                                                                                                          |

Open Actions by BIC

**GURNER™**

| SKETCHES ISSUED | PENDING SKETCHES |
|-----------------|------------------|
| 1               | 1                |
| 2               | 2                |
| 3               | 3                |
| 4               | 4                |
| 5               | 5                |
| 6               | 6                |
| 7               | 7                |
| 8               | 8                |
| 9               | 9                |
| 10              | 10               |
| 11              | 11               |
| 12              | 12               |
| 13              | 13               |
| 14              | 14               |
| 15              | 15               |
| 16              | 16               |
| 17              | 17               |
| 18              | 18               |
| 19              | 19               |
| 20              | 20               |
| 21              | 21               |
| 22              | 22               |
| 23              | 23               |
| 24              | 24               |
| 25              | 25               |
| 26              | 26               |
| 27              | 27               |
| 28              | 28               |
| 29              | 29               |
| 30              | 30               |
| 31              | 31               |
| 32              | 32               |
| 33              | 33               |
| 34              | 34               |
| 35              | 35               |
| 36              | 36               |
| 37              | 37               |
| 38              | 38               |
| 39              | 39               |
| 40              | 40               |
| 41              | 41               |
| 42              | 42               |
| 43              | 43               |
| 44              | 44               |
| 45              | 45               |
| 46              | 46               |
| 47              | 47               |
| 48              | 48               |
| 49              | 49               |
| 50              | 50               |
| 51              | 51               |
| 52              | 52               |
| 53              | 53               |
| 54              | 54               |
| 55              | 55               |
| 56              | 56               |
| 57              | 57               |
| 58              | 58               |
| 59              | 59               |
| 60              | 60               |
| 61              | 61               |
| 62              | 62               |
| 63              | 63               |
| 64              | 64               |
| 65              | 65               |
| 66              | 66               |
| 67              | 67               |
| 68              | 68               |
| 69              | 69               |
| 70              | 70               |
| 71              | 71               |
| 72              | 72               |
| 73              | 73               |
| 74              | 74               |
| 75              | 75               |
| 76              | 76               |
| 77              | 77               |
| 78              | 78               |
| 79              | 79               |
| 80              | 80               |
| 81              | 81               |
| 82              | 82               |
| 83              | 83               |
| 84              | 84               |
| 85              | 85               |
| 86              | 86               |
| 87              | 87               |
| 88              | 88               |
| 89              | 89               |
| 90              | 90               |
| 91              | 91               |
| 92              | 92               |
| 93              | 93               |
| 94              | 94               |
| 95              | 95               |
| 96              | 96               |
| 97              | 97               |
| 98              | 98               |
| 99              | 99               |
| 100             | 100              |

11/21 2

OVERVIEW   UNITS & ACTIONS   GANTT CHART   PHASES & MILESTONES

☐ Inc


● 1 — Design Phase

● **2 — Cost Phase**  
TARGET — 3 MONTHS  
Builder Pricing → Commercial Review → QS Certification

### 3 — DoV Phase

● **4 – Delivery**  
CONSTRUCTION & PLANNING  
Instructed to Hickory → DA Modification Submission → Modification Approval

Contractual milestone    ◆ Tracking step – complete    ◇ Tracking step – pending    ◇ Purchaser sign-off – pending    | Today    ⊕ Full unit detail

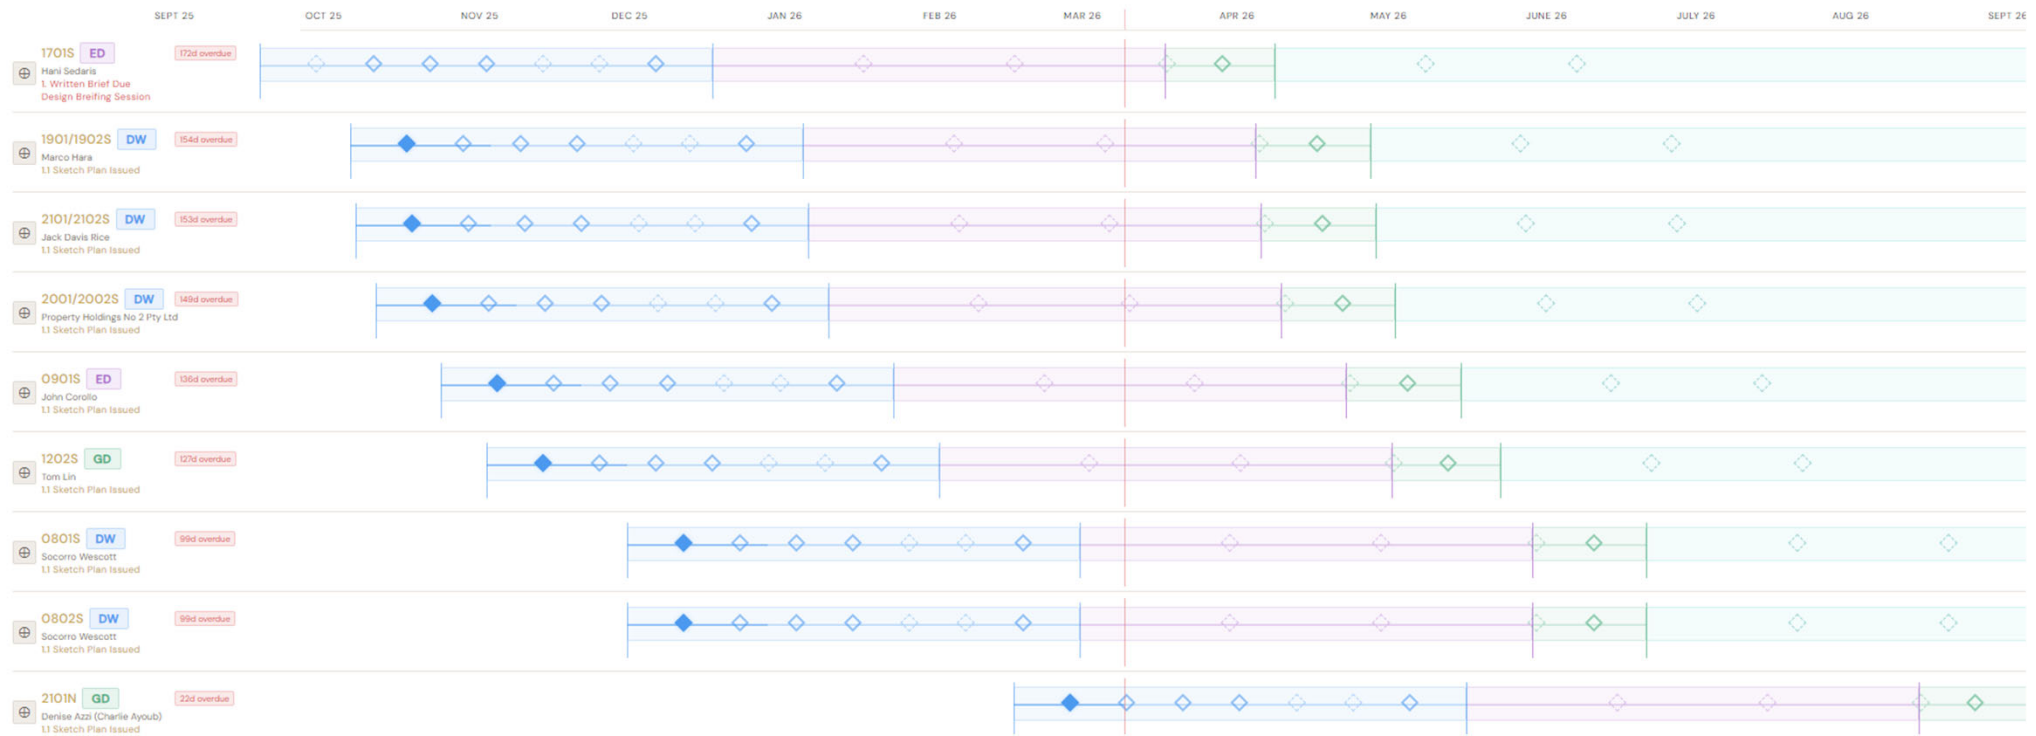

PHASES AND MILESTONES

GURNERTM

189 Kent Street  
SALUS PLACE — CUSTOMISATIONS TRACKER

SKETCHES ISSUED11/21

PENDING SKETCHES2

TODAY13 Mar 2026

OVERVIEW

UNITS & ACTIONS

GANTT CHART

PHASES & MILESTONES

● Phase 1 — Design

SC 68 — 90-DAY WINDOW

1

**Written Brief Due**

SC 68(b)(3)(A)

Purchaser submits written brief outlining requested bespoke changes to the vendor.  
[Within 20 business days of contract date](#)

Gurner Short Form — Phase 1

11

**Sketch Plan Issued**

Gurner Short Form — Phase 1

Design team prepares sketch plan. Buildability reviewed by GURNERTM team.  
[Week 1](#)

12

**Layout Confirmed — Letter Countersigned**

Gurner Short Form — Phase 2

Purchaser countersigns letter confirming layout is approved. No further layout changes accepted after this point.  
[Week 2](#)

13

**Cost Ranges Issued to Purchaser**

Gurner Short Form — Phase 3

Preliminary cost ranges for the bespoke design issued to purchaser for review and sign off before full design commences.  
[Week 2-4](#)

14

**Interiors & Finishes Confirmed by Purchaser**

Gurner Short Form — Phase 4

Finishes and bespoke drawings prepared. Purchaser confirms indicative costing of interiors and selections.  
[Week 4-8](#)

15

**FJC CAD Plans Issued for Pricing**

Gurner Short Form — Phase 4/5

Architect issues CAD plans incorporating agreed bespoke works for QS pricing.  
[Week 4-8](#)

16

**Final Pricing Issued to Purchaser**

Gurner Short Form — Phase 5

Final cost issued to purchaser. Final refinements based on costing resolved.  
[Week 8-12](#)

17

**Purchaser Confirms Final Pricing**

Gurner Short Form — Phase 5

Purchaser confirms intent to proceed based on final pricing.  
[Week 8-12](#)

18

**Design Period End**

SC 68(b)(3)(D)

End of the 90-day bespoke design period. Vendor may determine amendments unilaterally if no agreement reached by this date (SC 68(b)(ii)(F)).  
[3 months from contract date](#)

Contractual milestoneGurner internal step

● Phase 2 — Cost

POST DESIGN AGREEMENT (~3 MONTHS)

21

**Builder Budget Pricing**

Gurner Internal

Builder provides budget variation pricing and constructability input.  
[Post design agreement](#)

22

**Internal Commercial Review**

Gurner Internal

Internal Gurner confirmation of cost build-up and margin alignment.  
[Prior to QS certification](#)

23

**QS Cost Certification**

SC 68(b)(3)(G)

Vendor instructs a Quantity Surveyor to certify the cost impact of the agreed bespoke design changes. The QS determination is conclusive evidence of the Certified Variation Amount (SC 68(b)(ii)(H)).  
[After design agreed](#)

Contractual milestoneGurner internal step

● Phase 3 — Legal (DoV)

DEED OF VARIATION EXECUTION

31

**Internal DoV Approval**

Gurner Internal

Internal Gurner sign-off prior to issuing Deed of Variation. Gurner initials each page before issue.  
[After QS certification](#)

32

**DoV Issued to Purchaser**

SC 68(b)(3)(J)

Vendor drafts and issues Deed of Variation formally documenting agreed bespoke works, amended plans and specifications, and price adjustment.  
[After QS certification](#)

33

**Purchaser Executes DoV**

SC 68(b)(3)(K)

Purchaser must execute the Deed of Variation within 14 days. Note: contract is automatically amended under SC 68(c) regardless of whether the purchaser executes the DoV.  
[Within 14 days of issue, or Date for Completion \(whichever earlier\)](#)

Contractual milestoneGurner internal step

34

**Deposit Top-Up Paid**

SC 68(b)(3)(L)

Deposit amended to 10% of revised price. Purchaser pays outstanding balance — or vendor refunds overpayment if price decreased — within 10 business days of the Deed of Variation date.  
[Within 10 business days of DoV date, or Date for Completion \(whichever earlier\)](#)

● Phase 4 — Delivery

CONSTRUCTION & PLANNING APPROVALS

41

**Instructed to Hickory**

Internal programme

Builder instructed to proceed with bespoke works.  
[Post DoV execution](#)

42

**Planning / DA Modification Submission**

Internal programme

Recommended latest date to submit planning modification application to the relevant Consent Authority.  
[Upon DoV execution](#)

43

**Modification Approval**

Clause 33 / SC 68(e)

Deadline by which s.4.55 DA modification approval must be obtained. Delivery of consolidated/customised lot is conditional on this approval (SC 68(e)).  
[Fixed contractual sunset date](#)

Contractual milestoneGurner internal step

LIVE DASHBOARD LINK – PASSWORD: Kent189

[https://gurnerwmorris.github.io/189-Kent\\_Customisations/](https://gurnerwmorris.github.io/189-Kent_Customisations/)

---
